Power Grid Bangladesh PLC
National Load Dispatch Center (NLDC)
System Summary Report


Date : 25-10-2026


Power Supply Scenario

Day Peak Generation	14192.49	MW	12:00 Hr.	Energy Generated	334.16394	MKWHr.
Day Peak Demand	14210.49	MW	12:00 Hr.	Energy Unserverd	0.66600	MKWHr.
Evening Peak Generation	15790.97	MW	18:00 Hr.	Energy Demand	334.82994	MKWHr.
Evening Peak Demand	16000.97	MW	18:00 Hr.	Maximum Temperature	34.20	°C
Minimum Generation of the Day	11624.8	MW	06:00 Hr.	Total Gas Supplied	851.88	MMCFD
Maximum Generation of the Day	15790.97	MW	18:00 Hr.	Production Cost per KWHr	7.45341	Tk.

Zone-wise Generation Summary (MKWHr.)

	Gas	Coal	HFO	HSD	Hydro	Solar	Import	Wind	**Total**
Dhaka Zone	36.85	0.00	12.90	0.00	0.00	0.22	0.00	0.00	0.00
Chattogram Zone	5.35	53.03	6.11	0.00	2.24	0.12	0.00	0.12	0.00
Cumilla Zone	24.72	0.00	4.23	0.00	0.00	0.39	1.58	0.00	0.00
Mymensingh Zone	0.07	0.00	4.10	0.00	0.00	0.49	0.00	0.00	0.00
Sylhet Zone	36.00	0.00	0.00	0.00	0.00	0.08	0.00	0.00	0.00
Khulna Zone	0.00	26.40	0.43	0.00	0.00	0.51	22.68	0.00	0.00
Barishal Zone	2.71	54.92	1.31	0.00	0.00	0.00	0.00	0.00	0.00
Rajshahi Zone	6.38	0.00	2.55	0.00	0.00	1.62	23.37	0.00	0.00
Rangpur Zone	0.00	0.00	1.11	0.00	0.00	1.59	0.00	0.00	0.00
Total	112.06	134.35	32.73	0.00	2.24	5.02	47.64	0.12	334.16

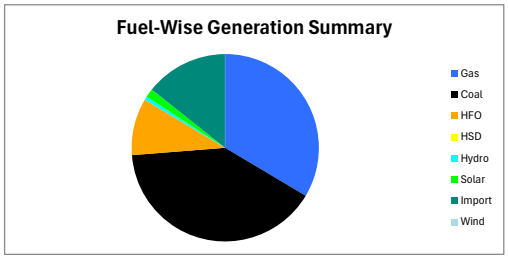

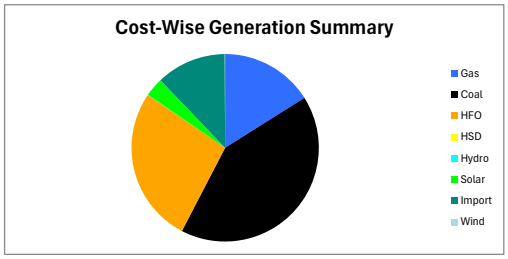

Production Cost (Tk.)

Fuel	**Tk.**	**Fuel**	**Tk.**
Gas	400216748.7	Hydro	223735.6
Coal	1035483919	Solar	80931072.12
HFO	670497812.6	Import	301585499.9
HSD	0	Wind	1721491.2

Total: 249,06,60,278 Tk.

E-W Interconnector & Import Scenario

Energy Flow from East to West:	KWHr:	0	Import through HVDC C/B Interconnector:	MKWHr:	21.768727	Peak Hr Flow	891.00 MW at 18:00 hrs.
Energy Flow from West to East:	KWHr:	49633818.18	Import through Adani C/B Interconnector:	MKWHr:	23.372728	Peak Hr Flow	1113.89 MW at 18:00 hrs.
Power Flow during Peak Demand (W-E):	MW:	2111	Import through Cumilla C/B Interconnector:	MKWHr:	1.58496	Peak Hr Flow	84.00 MW at 18:00 hrs.
Maximum Power Flow (W-E):	MW:	2643	Total Import through C/B Interconnector:	MKWHr:	46.726415	Peak Hr Flow	2088.89 MW at 18:00 hrs.

Zone-wise Load-shed and Demand Summary (MW) at evening peak Hour (18:00 Hr.)

Zone	**Load-Shed**	**Demand**
Dhaka	76	6055
Chattogram	0	1670
Cumilla	0	1558
Mymensingh	120	1334
Sylhet	0	706
Khulna	0	1704
Barishal	0	455
Rajshahi	5	1417
Rangpur	0	871
Total	**201**	**15770**

Status of unavailable Power Plant

Planned S/D			**Forced S/D**		
Sl	Plant Name	Capacity	Sl	Plant Name	Capacity
1	Baghabari 100 MW GTPP	100	1	Fenchugonj CCPP Phase-2 ST	35
2	Barapukuria TPP Unit-2	85	2	Karnaphuli Hydro PP Unit-1	40
3	Siddhirgonj 210 MW TPP	115	3	Karnaphuli Hydro PP Unit-2	40
			4	Karnaphuli Hydro PP Unit-3	50
			5	Sylhet 225 MW CCPP ST	89
	Total	300		Total	254
	Total Unavailable Capacity	**554**			

Event Summary

Outage Time	Restoration Time	Description of Event	Description of Event
08:11	12:28	Kaliakoir 400/230/132kV S/S 400kV Bus 1 Scheduled S/D Due to Annual Maintenance for Kaliakoir SS. And DS-1301S Alignment correction for G2G project.	
08:13	17:12	Bogura-Sirajganj 230 kV Ckt-1 Scheduled S/D from Bogura 230/132kV end Due to Annual Maintenance work,	

Power Grid Bangladesh PLC
National Load Dispatch Center (NLDC)
System Summary Report

Date : 25-10-2026

08:17	15:12	Rajbari 132/33kV S/S Transformer-2 LT Scheduled S/D Due to Annual maintenance work.	
08:18	15:12	Rajbari 132/33kV S/S Transformer-2 HT Scheduled S/D Due to Annual maintenance work.	
08:22	16:00	Aminbazar-Mirpur 132kV Ckt-1 Scheduled S/D from Aminbazar 400/230/132kV end Due to Annual maintenance	
	08:28	Kushtia 132/33kV S/S 132 KV Bus-B is restored.	
08:29	16:39	Chauddagram-Cumilla(S) 132 kV Ckt-1 Scheduled S/D from Cumilla(S) 132/33kV end Due to বার্ষিক সংরক্ষন কাজ and from Chauddagram 132/33kV end Due to annual maintenance	
08:30	17:05	Chattak-Sunamganj 132 kV Ckt-1 Scheduled S/D from Sunamganj 132/33kV end Due to Due to annual maintenance and from Chhatak 132/33kV end Due to Annual Maintanance Work	
08:34	17:31	Kushtia 132/33kV S/S T-3 LT Project Work S/D Due to Project work	
08:34	16:35	Ghatail-Tangail 132kV Ckt-1 Scheduled S/D from Muktagacha 132/33kV end Due to Annual Maintenance.	
08:35	17:30	Kushtia 132/33kV S/S T-3 HT Project Work S/D Due to Project work	
08:45		Kushtia 132/33kV S/S 132 KV Bus-A Project Work S/D Due to Project work	
08:55	16:11	Sylhet_(South) 132/33kV S/S Sylhet (S)-Biyanibazar 132KV Ckt-2 Scheduled S/D Due to Annual Maintenance	
08:55	16:20	Fenchuganj-Sylhet (T at Bianibazar) 132kV Ckt-2 Scheduled S/D from Beanibazar 132/33kV end Due to Annual Maintenance	
08:57	15:36	Goalpara 132/33kV S/S Bus 1 Scheduled S/D Due to Annual Maintenance.	
09:07	15:21	Saidpur 132/33kV S/S TR-5 (434T) HT Scheduled S/D Due to Annual maintenance	
09:07	15:22	Saidpur 132/33kV S/S TR-5 (434T) LT Scheduled S/D Due to Annual maintenance	
10:04	16:14	Chowmuhani-Ramganj 132 kV Ckt-2 Scheduled S/D from Chowmuhani 230/132/33kV end Due to Due to dismantle ERS tower of chowmuhani-ramgonj tower shifting work.	
10:09		Barapukuria(N)-Rangpur 230kV Ckt-2 Project Work S/D from Barapukuria(N) 230kV end Due to 230kV XLPE Cable termination work.	
10:12		Barapukuria(N)-Rangpur 230kV Ckt-1 Project Work S/D from Barapukuria(N) 230kV end Due to 230kV XLPE Cable termination work.	
10:28	18:15	Purbasadipur-Saidpur 132kV Ckt-1 Scheduled S/D from Purbasadipur 230/132/33kV end Due to CB Replacement work at Saidpur 132/33 kV Grid Sub-Station end.	
11:47		Sylhet 225 MW CCPP Tripped with remarks:- ST	
11:48		Sylhet 225 MW CCPP Synchronized with remarks:- STG (This is False SMS)	
	11:54	Gopalganj 132/33kV S/S T2 HT is restored.	
	11:55	Gopalganj 132/33kV S/S T2 LT is restored.	
12:00		Day Peak Generation: 14192 MW.	
12:39	13:57	Gopalganj 132/33kV S/S Transformer-03 LT Scheduled S/D Due to DS to main bus clamp red hot maintenance	10.0MW load interrup.
12:40	13:56	Gopalganj 132/33kV S/S Transformer-03 HT Scheduled S/D Due to DS to main bus clamp red hot maintenance	10.0MW load interrup.
13:02	13:53	Manikganj 132/33kV S/S 132/33 kV Transformer GT-4 (50/75 MVA) LT Scheduled S/D Due to GT4 X-Former 33 KV side temperature rise.	
13:02	13:51	Manikganj 132/33kV S/S 132/33 kV Transformer GT-4 (50/75 MVA) HT Scheduled S/D Due to GT4 X-Former 33 KV side temperature rise.	
	13:22	Bogura 230/132kV S/S 132KV Main 1 is restored.	
	13:31	Bogura South-Confidence 132 kV Ckt-2 is restored.	
	14:22	Kaliakoir-Shomvuganj 400kV Ckt-1 was charged from Kaliakoir end for the first time	
15:16	17:19	Haripur 230/132kV S/S Auto TR-1 LT Forced S/D Due to Oil leakage.	
15:16	17:19	Haripur 230/132kV S/S Auto TR-1 HT Forced S/D Due to Oil leakage.	
15:30		Meghnaghat CCPP(Summit) Synchronized with remarks:- Gt-2	
15:30		Meghnaghat CCPP(Summit) GT-2 Synchronized with remarks:- GT-2 synchronized at 15:30 hrs as per NLDC demand.	

Power Grid Bangladesh PLC
National Load Dispatch Center (NLDC)
System Summary Report

Date : 25-10-2026

17:05	18:55	Madanganj 132/33kV S/S Madanganj -DPDC Char sayedpur 132k Ckt-1 Forced S/D
	17:15	Patuakhali 132/33kV S/S 405T (T-1) HT is restored.
	17:17	Patuakhali 132/33kV S/S 405T (T-1) LT is restored.
19:07		Meghnaghat CCPP(Summit) ST Synchronized with remarks:- ST synchronized at 19:07 hrs as per NLDC demand
19:07		Meghnaghat CCPP(Summit) Synchronized with remarks:- ST
	19:24	Payra 400/132/33kV S/S 132/33 kV Transformer-04 HT is restored.
22:38		Meghnaghat CCPP(Summit), FGMO is ON with remarks:- CCPP put into FGMO at 21:36 hrs as per NLDC demand.
23:38		Meghnaghat CCPP(Summit) GT-1 Synchronized with remarks:- GT-1 synchronized as per NLDC request
06:00		Minimum Generation: 12235 MW.
06:06		Payra 1320 MW Shutdown with remarks:- unit-1
06:50		Payra 1320 MW Synchronized with remarks:- false
06:55		Barishal 132/33kV S/S 132 kV Capacitor Bank Scheduled S/D Due to Annual Maintenance.
07:06		Patuakhali 132/33kV S/S 415T (T-2) LT Scheduled S/D Due to Annual maintenance work
07:07		Patuakhali 132/33kV S/S 415T (T-2) HT Scheduled S/D Due to Annual maintenance work
07:29		Aminbazar-Mirpur 132kV Ckt-1 Scheduled S/D from Aminbazar 400/230/132kV end Due to For annual maintenance 2nd days.
07:37		Barishal 230/132kV S/S 230kV BUS Scheduled S/D Due to Annual maintenance
07:43		Ishwardi-Rooppur 132kV Ckt-1 Scheduled S/D from Ishurdi 132/33kV end Due to A/M
07:54		Rajbari 132/33kV S/S Transformer-3 LT Scheduled S/D Due to Annual maintenance work 2026
07:55		Rajbari 132/33kV S/S Transformer-3 HT Scheduled S/D Due to Annual maintenance work 2026

Sub-Divisional Engineer
Network Operation Division

Executive Engineer
Network Operation Division

Superintendent Engineer
Network Operation Division
